

50th Way Flood Reduction Project – Construction Update

August 2016

Construction on NE 50th Way has begun; Project work hours 7 a.m. – 5 p.m.

Construction has begun in Zone 4 near West Lake Sammamish Parkway and NE 50th Way and will continue through Zones 3 and 2, ending in Zone 1. Work is expected to take approximately three months.

As work gets underway, construction work hours are now typically 7 a.m. – 5 p.m. Monday through Thursday. Construction work will happen on Fridays as needed. We will communicate with residents if work is planned outside typical hours.

About the project

The 50th Way Flood Reduction project will install 520 feet of new pipes to direct stormwater away from the 50th Way Stream and reduce flooding along NE 50th Way during heavy rain events.

What to expect during construction:

- Work hours typically between 7 a.m. and 5 p.m. Monday through Thursday, Friday work as needed
- Tree removal and replacement
- Temporary lane closures
- Noise, dust and vibrations
- Increased truck traffic
- Progress updates and notification prior to work scheduled outside of normal work hours

50th Way Flood Reduction Project Updated Construction Map

Zone 4:

- Tree and shrub removal
- Place new pipe and repair driveway

Zone 3:


- Remove invasive plants and replace with native species

Zone 1:

- Saw cut asphalt, remove curb
- Dig trench
- Place new pipe and catch basin
- Backfill trench
- Repair street, curb and sidewalk

Zone 2:

- Saw cut asphalt, remove curb
- Dig trench
- Place new pipe and catch basin
- Backfill trench
- Repair street, curb and sidewalk

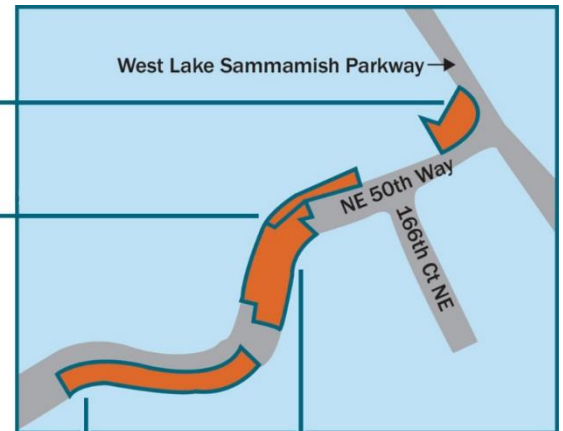

More questions?

www.redmond.gov/toshcreek and click on 50th Way Flood Reduction

Project contact information

Please direct questions and concerns to the 50th Way Flood Reduction project manager, Bassam Al-Ali:

Phone: 425-556-2743 | **Email:** Bal-ali@redmond.gov

How to stay informed and involved!

Visit www.redmond.gov/ToshCreek | Email Tosh@redmond.gov | Call 425-556-2738
