# **Two-way Street Conversion**



This project will upgrade utilities and convert both Redmond Way and Cleveland Street to two-way traffic, creating better access for residents and businesses.

O Location: Redmond Way and Cleveland St from 160th Ave NE to Avondale Way

Project Phase: Under construction

**Estimated Timeline:** Design 2013-2015, Construction June 2016 through end of 2017

Contact: Jill Smith, Downtown Outreach, 425-556-2448 • Lisa Singer, Project Manager, 425-556-2723


The conversion will make Downtown easier to navigate and more connected, whether you are driving, walking, biking, or taking transit. Cleveland Street is designated as Redmond's signature "main street" while Redmond Way will carry the majority of traffic as the main arterial through Downtown. This project is the completion of the planned transportation grid in Downtown, which included the sequencing of six major roadway and utility infrastructure projects over the past six years.

# The following work will occur at the eleven intersections:


- Replacing old utilities (water, storm)
- New traffic signals, lighting, and sidewalks
- Undergrounding of overhead power and communications
- Paving and landscaping
- New plazas near Anderson Park

#### Work between the intersections includes:

- Reconfiguring lanes
- Updating street signs
- Remaining sidewalk and parking improvements between intersections will be constructed later as private development occurs

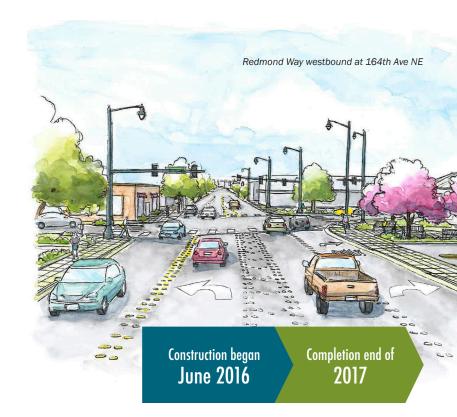

Maintaining access to businesses and adjacent properties will be a priority during the project.



# **Project Timeline:**



## **Project Costs:**

Total:\$27.0 millionCity General & Utility Funds:\$ 2.8 millionOther Funding:\$24.2 million

### **Recent Activities:**

- · Coordinating weekly with adjacent developers and utility companies on construction activities, schedules, and access.
- Redmond Way reopened to two lanes in November, with occasional daytime closures to one lane.
- Current construction phase is nearly complete with the installation of new sewer main on Redmond Way between 168th and Avondale Way.

# What's Happening Next:

- Project impacts are constantly changing. Find updates and the option to sign up for project and construction news below.
- Undergrounding of power lines, concrete curbs and driveways, and continued work on the new signal systems.

# **Neighborhood Impacts:**

- Construction impacts mostly occur during the daytime and may include lane closures and some construction noise.
  However, occasional night work is anticipated.
- Traffic impacts from construction activities include the temporary closure of the south end of 168th Ave NE during construction. Businesses impacted by temporary cut overs of utility work will be notified.
- Please stay aware of and follow changing pedestrian access routes through the construction zones.



#### Get Involved:

Sign up for traffic alerts and get the latest project updates at *redmond.gov/enews*. Just make sure to select "Traffic Alerts" and "Downtown Construction Updates" in the subscriber options menu after entering your email.

#### Please support downtown businesses!

Eat, sip and shop at the variety of businesses that call Downtown Redmond home. You can find a directory of businesses at www.ExperienceRedmond.com. Or for more information on current and upcoming projects, visit: redmond.gov/downtown



#### **Related News:**

See a KIROTV story on the Two-way Street Conversion at kiro.tv/RedmondStreets
